


- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Contract DC/2019/10 - YLEPP - Main Works for Stage 1

Monthly Progress Report No. 41- 3MRP (Mar 24)

Project ID : DWP36_240416
 Layout : DC201910 MPR41-3MRP
 Page 4 of 8

Monthly Progress Report - 3MRP			
Date	Revision	Checked	Approved
31-Mar-24	Rev. 0		

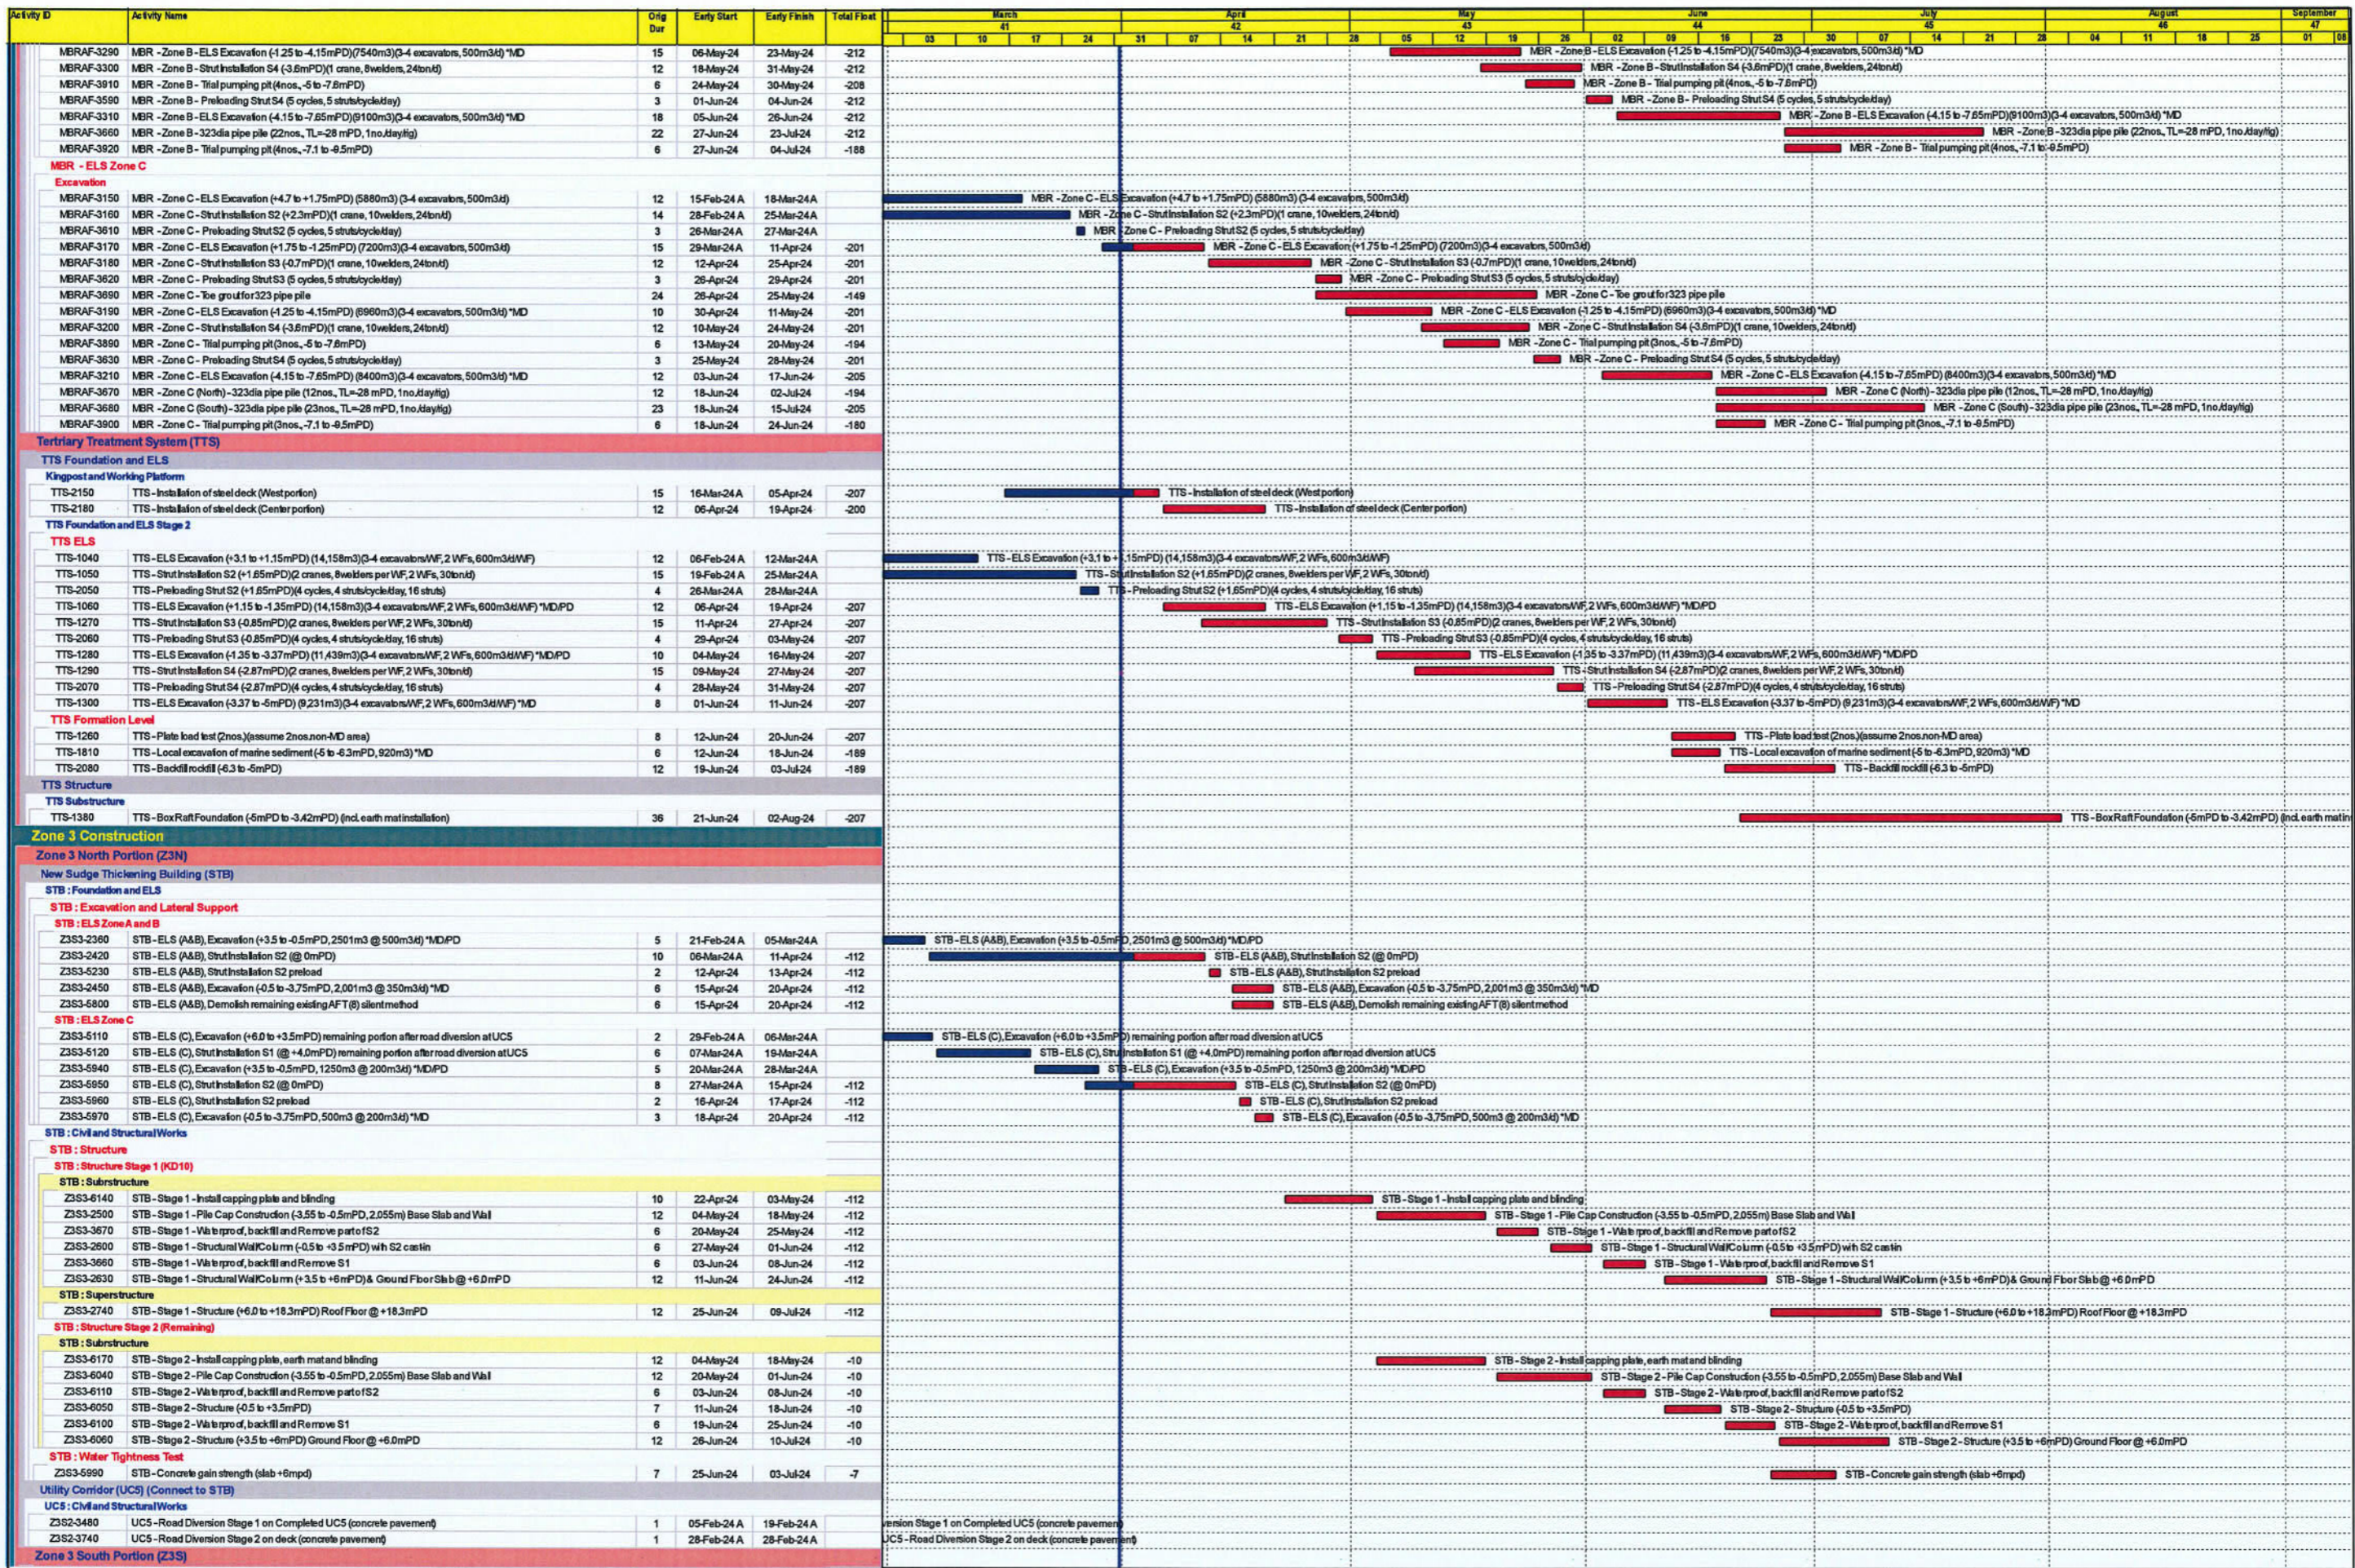

- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Contract DC/2019/10 - YLEPP - Main Works for Stage 1

Monthly Progress Report No. 41- 3MRP (Mar 24)

Project ID : DWP36_240416
 Layout : DC201910 MPR41-3MRP
 Page 7 of 8

Monthly Progress Report - 3MRP			
Date	Revision	Checked	Approved
31-Mar-24	Rev. 0		

Activity ID	Activity Name	Orig Dur	Early Start	Early Finish	Total Float	March				April				May				June				July				August				September	
						03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25
Sludge Digester No. 1-3 (SD1-3) SD1-3: Foundation and ELS SD1-3: Sheetpiling, Kingpost, Monitoring and pumping Z3S3-6100 Sludge Digester No.1-3 - Pumping test* assume reading taking during CNY Z3S3-6160 Sludge Digester No.1-3 - Add to rail routing for BHI settlement control SD1-3: Excavation and Strut Installation SD1-3: ELS Z3S3-2110 Sludge Digester No.1-3 - ELS Excavation (+5.0 to +4.3mPD, 4168m3 @ 1000m3/d) Z3S3-2140 Sludge Digester No.1-3 - Strut Installation S1 (+4.8mPD) Z3S3-2150 Sludge Digester No.1-3 - ELS Excavation (+4.3 to +1.8mPD, 6130m3 @ 1000m3/d) Z3S3-2190 Sludge Digester No.1-3 - Strut Installation S2 (+2.3mPD) Z3S3-5730 Sludge Digester No.1-3 - Preloading Strut S2 (+2.3mPD)(4 cycle, 5 struts/cycle/day, 16 struts) Z3S3-2200 Sludge Digester No.1-3 - ELS Excavation (+1.8 to -0.7mPD, 6130m3 @ 1000m3/d)*MD Z3S3-2210 Sludge Digester No.1-3 - Strut Installation S3 (-0.2mPD) Z3S3-5740 Sludge Digester No.1-3 - Preloading Strut S3 (-0.2mPD)(4 cycle, 5 struts/cycle/day, 16 struts) Z3S3-2220 Sludge Digester No.1-3 - ELS Excavation (-0.7 to -3.2mPD, 6130m3 @ 1000m3/d)*MD Z3S3-2230 Sludge Digester No.1-3 - Strut Installation S4 (-2.7mPD) Z3S3-5750 Sludge Digester No.1-3 - Preloading Strut S4 (-2.7mPD)(4 cycle, 5 struts/cycle/day, 16 struts) Z3S3-2240 Sludge Digester No.1-3 - ELS Excavation (-3.2 to -5.5mPD, 5640m3 @ 1000m3/d) Z3S3-3600 Sludge Digester No.1-3 - Strut Installation S5 (-5.0mPD) Z3S3-5760 Sludge Digester No.1-3 - Preloading Strut S5 (-5.0mPD)(4 cycle, 5 struts/cycle/day, 16 struts) Z3S3-3610 Sludge Digester No.1-3 - ELS Excavation (-5.5 to -7.5mPD, 4904m3 @ 1000m3/d) Z3S3-3620 Sludge Digester No.1-3 - Strut Installation S6 (-7mPD) Z3S3-5770 Sludge Digester No.1-3 - Preloading Strut S6 (-7mPD)(4 cycle, 5 struts/cycle/day, 16 struts) Z3S3-3630 Sludge Digester No.1-3 - ELS Excavation (-7.5 to -9.0mPD, 3678m3 @ 1000m3/d)																															
Biogas Holder No. 1 (BH1) BH1: E&M Installation ATALZ3BH-2455 BH No.1 - Jack installation ATALZ3BH-2465 BH No.1 - Tank wall (2nd to 3rd Ring) and tank mounting ring construction and welding ATALZ3BH-2475 BH No.1 - Tank wall (4th to 5th Ring) construction and welding ATALZ3BH-1010 BH No.1 - Installation of pipework and instrumentation in Biogas Holder Valve Chamber No.4 ATALZ3BH-1020 BH No.1 - Instrumentation ATALZ3BH-1030 BH No.1 - Installation of Biogas Booster Pump No.1 & 2 ATALZ3BH-1040 BH No.1 - Electrical works (Cable wiring, termination, lightning arrestor)(To all power source until LVSB@STB energiz) ATALZ3BH-2485 BH No.1 - Disk assembly inside tank, raise disk, painting on both side ATALZ3BH-2495 BH No.1 - Membrane lining and wooden plank installation BH1: Diversion Works Z3S7-2060 BH No.1 - Temporary system and associated pipework for switchover to new BH1 for decommission of GH2 Utility Corridor and Pipe Portal (UCPP) Utility Corridor No.1 (UC1) UC1: Predrilling Works Z3S5UC1-2180 UCPP - Predrill UC&PP-PD2 Z3S5UC1-2200 UCPP - Predrill UC&PP-PD6																															



- Remaining Level of Ef...
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ ◆ Milestone

Contract DC/2019/10 - YLEPP - Main Works for Stage 1

Monthly Progress Report No. 41- 3MRP (Mar 24)

Project ID : DWP36_240416
 Layout : DC201910 MPR41-3MRP
 Page 8 of 8

Monthly Progress Report - 3MRP

Date	Revision	Checked	Approved
31-Mar-24	Rev. 0		
